LNER

Activity, people & shot history



10	156	1902
TIMELINES	SHOTS · INCLUDING HIDDEN	PRODUCTION EVENTS

This report covers 156 shots across 10 timelines, including 46 hidden shots. It follows task assignments, status changes and recorded conform/render updates.

10 tasks approved; 183 tasks done; 22 tasks awaiting approval; 57 tasks in other open states.

Inside: producer overview · artist workboard · activity charts · shot records

Recorded activity: 05 Jan 2026 – 20 Mar 2026.

Generated 29 Oct 2026, 16:51 GMT.


Producer overview

Who holds the work, what is complete, and what still needs attention.

All timelines · includes hidden shots and tasks. Counts may differ from the web overview with hidden items switched off.


79 ACTIVE TASKS	193 COMPLETED	60 NO ASSIGNED ARTIST
8 IN PROGRESS	22 AWAITING APPROVAL	7 ACTIVE ARTISTS

Work by artist

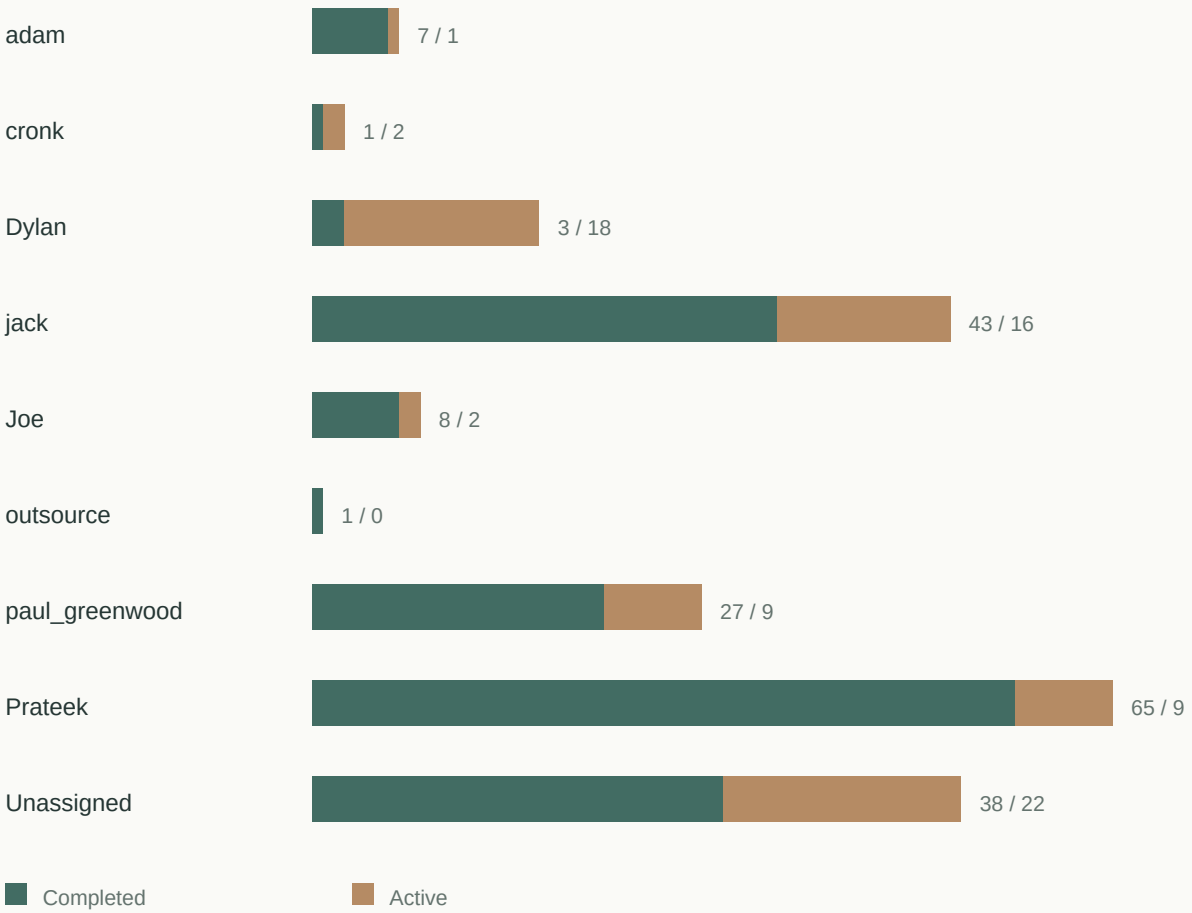

Bars show current assigned tasks. Labels give completed / active counts; completed means Approved or Done.

Current task status

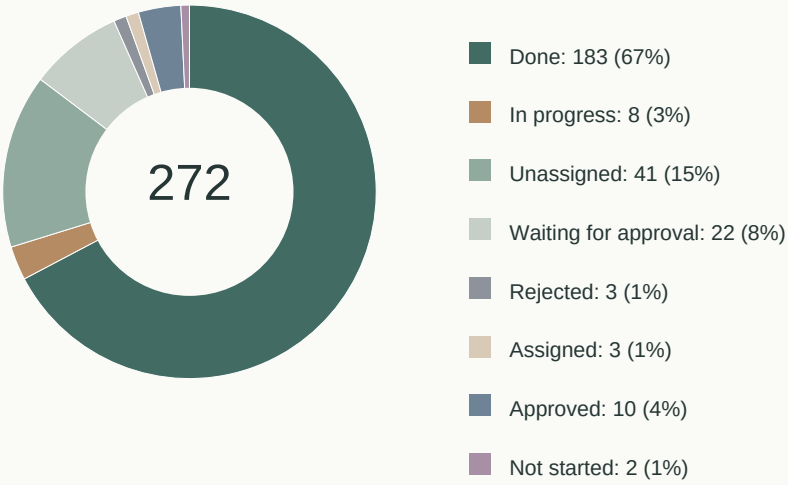

Tasks without an artist may already be approved. Assignment describes recorded responsibility, not proof of authorship.


Artist workboard

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

adam

8 tasks · 1 active · 7 completed

ACTIVE / NEEDS ATTENTION




cna010

Considerations B1

Comp · assigned

COMPLETED




cna030

Considerations B1

Comp · done

COMPLETED



cna040

Considerations B1

Comp · done

COMPLETED



cna050


Considerations B1

Comp · done

adam · continued

8 tasks · 1 active · 7 completed

COMPLETED




cna060

Considerations B1

Comp · done

COMPLETED



cna070

Considerations B1

Comp · done

COMPLETED



sho020

new shots

Camera match · done

COMPLETED



sho040

new shots

Camera match · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

cronk

3 tasks · 2 active · 1 completed

ACTIVE / NEEDS ATTENTION · HIDDEN SHOT



lnr020

60s cut 7

painting — paint the car · unassigned

ACTIVE / NEEDS ATTENTION · HIDDEN SHOT



lnr040

60s cut 7

roto face · in progress

COMPLETED · HIDDEN SHOT



lnr020

60s cut 7

New Task · done

Dylan

21 tasks · 18 active · 3 completed

ACTIVE / NEEDS ATTENTION · HIDDEN SHOT



lnr020

60s cut 7

test · assigned

ACTIVE / NEEDS ATTENTION



spo040

Spotting

Comp · unassigned

ACTIVE / NEEDS ATTENTION



spo050

Spotting

Rod paint · unassigned

ACTIVE / NEEDS ATTENTION



spo060

Spotting

Rod paint · unassigned

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Dylan · continued

21 tasks · 18 active · 3 completed

ACTIVE / NEEDS ATTENTION




spo080

Spotting

carrrage · unassigned

ACTIVE / NEEDS ATTENTION




spo100

Spotting

carrage · unassigned

ACTIVE / NEEDS ATTENTION



spo120

Spotting

Comp · unassigned

ACTIVE / NEEDS ATTENTION



tvc020

TrainVsCar

greenscreen · waiting for approval

Dylan · continued

21 tasks · 18 active · 3 completed

ACTIVE / NEEDS ATTENTION



tvc040

TrainVsCar

paint · waiting for approval

ACTIVE / NEEDS ATTENTION



tvc060

TrainVsCar

paint · waiting for approval

ACTIVE / NEEDS ATTENTION



tvc080

TrainVsCar

Paint · waiting for approval

Paint — fix roto · waiting for approval

ACTIVE / NEEDS ATTENTION



tvc100

TrainVsCar

Paint · waiting for approval

Paint — fix ro · waiting for approval

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Dylan · continued

21 tasks · 18 active · 3 completed

ACTIVE / NEEDS ATTENTION



tvc120

TrainVsCar

Paint · waiting for approval

ACTIVE / NEEDS ATTENTION



tvc140

TrainVsCar

Paint · in progress

ACTIVE / NEEDS ATTENTION



tvc160

TrainVsCar

Paint · in progress

ACTIVE / NEEDS ATTENTION



tvc180

TrainVsCar

Paint · in progress

Dylan · continued

21 tasks · 18 active · 3 completed

COMPLETED



lnr230

60s cut 7

remove apple logo [hidden task] · done

COMPLETED



lnr250

60s cut 7

sign · done

COMPLETED



tvc020

TrainVsCar

Roto — fix cam stab · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

jack

59 tasks · 16 active · 43 completed

ACTIVE / NEEDS ATTENTION




cat010

CatchingUp

Comp · unassigned

ACTIVE / NEEDS ATTENTION



cat020

CatchingUp

Comp · unassigned

ACTIVE / NEEDS ATTENTION




cat030

CatchingUp

Comp · unassigned

ACTIVE / NEEDS ATTENTION



cat040


CatchingUp

Comp · unassigned

jack · continued

59 tasks · 16 active · 43 completed

ACTIVE / NEEDS ATTENTION




cnb010

Considerations B2

Match move · unassigned

ACTIVE / NEEDS ATTENTION




cnb030

Considerations B2

Match move · unassigned

ACTIVE / NEEDS ATTENTION



cnb040

Considerations B2

Match move · unassigned

ACTIVE / NEEDS ATTENTION



cnb050

Considerations B2

Match move · unassigned

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

jack · continued

59 tasks · 16 active · 43 completed

ACTIVE / NEEDS ATTENTION



lnr010

60s cut 7

make plane bigger [hidden task] · unassigned

ACTIVE / NEEDS ATTENTION



lnr070

60s cut 7

remove people · unassigned

ACTIVE / NEEDS ATTENTION



lnr170

60s cut 7

add lady — suitcase · not started

ACTIVE / NEEDS ATTENTION



sho070

new shots

Roto · unassigned

Comp · unassigned

jack · continued

59 tasks · 16 active · 43 completed

ACTIVE / NEEDS ATTENTION




sho080

new shots

Roto · unassigned

Comp · unassigned

ACTIVE / NEEDS ATTENTION



spo120

Spotting

Match move — dont need match move use other plate · unassigned

COMPLETED



cat010

CatchingUp

Camera match · done

COMPLETED



lnr010

60s cut 7

match move [hidden task] · done

set scan — photo geo [hidden task] · done

prep 3d [hidden task] · done

fix roto [hidden task] · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

jack · continued

59 tasks · 16 active · 43 completed

COMPLETED



lnr100

60s cut 7

split plate · done

Comp · done

car branding/number plate · done

COMPLETED



lnr110

60s cut 7

puppet roto [hidden task] · done

COMPLETED



lnr150

60s cut 7

puppet roto [hidden task] · done

COMPLETED



lnr190

60s cut 7


train 3d [hidden task] · done

key [hidden task] · done

jack · continued

59 tasks · 16 active · 43 completed

COMPLETED



lnr200

60s cut 7

tilt background train · done

COMPLETED



lnr210

60s cut 7

camera match · done

COMPLETED



lnr220

60s cut 7

camera match · done

cg carriage · done

puppet roto · done

rod paint · done

COMPLETED



lnr250

60s cut 7

camera match [hidden task] · done

remove cup [hidden task] · done

split [hidden task] · done

set up comp [hidden task] · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

jack · continued

59 tasks · 16 active · 43 completed

COMPLETED



lnr270

60s cut 7

camera match [hidden task] · done

COMPLETED



lnr280

60s cut 7

match move [hidden task] · done

make field nicer [hidden task] · done

COMPLETED



lnr290

60s cut 7

rod clean up [hidden task] · done

splits — reverce dad [hidden task] · done

COMPLETED



lnr320

60s cut 7

cg carriage — NEEDED FOR BOTH ENDS · done

jack · continued

59 tasks · 16 active · 43 completed

COMPLETED



lnr330

60s cut 7

keying issue [hidden task] · done

COMPLETED



sho010

new shots

Match move · done

COMPLETED



spo040

Spotting

Camera match · done

COMPLETED



spo080

Spotting

Match move · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

jack · continued

59 tasks · 16 active · 43 completed

COMPLETED



spo090

Spotting

Camera match · done

COMPLETED



spo100

Spotting

Match move · done

COMPLETED



tip020

Tips

Match move [hidden task] · done

COMPLETED



tip040

Tips

Match move · done

jack · continued

59 tasks · 16 active · 43 completed

COMPLETED



tip050

Tips

Match move · done

COMPLETED



tip080

Tips

Match move · done

COMPLETED



tip090

Tips

Match move · done

COMPLETED



tip120

Tips

Match move · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

jack · continued

59 tasks · 16 active · 43 completed

COMPLETED



tip140

Tips

Match move · done

COMPLETED



tip150

Tips

Match move · done

COMPLETED



tvc020

TrainVsCar

match camera · done

Joe

10 tasks · 2 active · 8 completed

ACTIVE / NEEDS ATTENTION



lnr170

60s cut 7

puppet roto — Harvey [hidden task] · waiting for approval

finish o · in progress

COMPLETED



lnr010

60s cut 7

remove car branding [hidden task] · done

number plates [hidden task] · done

reduce density of trees [hidden task] · done

COMPLETED



lnr140

60s cut 7

refine comp [hidden task] · done

check eleanor roto [hidden task] · done

contact shadows for eleanor [hidden task] · done

eleanor sharpening [hidden task] · done

eleanor shadow on floor [hidden task] · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

outsource

1 task · 0 active · 1 completed

COMPLETED



lnr170

60s cut 7

Roto · done

paul_greenwood

36 tasks · 9 active · 27 completed

ACTIVE / NEEDS ATTENTION



cat010

CatchingUp

bg env · unassigned

ACTIVE / NEEDS ATTENTION



lnr280

60s cut 7

NEW BG BACKGROUND — RENDERED · waiting for approval

ACTIVE / NEEDS ATTENTION



lnr290

60s cut 7

Add text above door — Need Rendering · waiting for approval

ACTIVE / NEEDS ATTENTION



lnr300

60s cut 7

bg env — v03 reverse · rejected

NEW BG RENDER — RENDERERD · waiting for approval

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

paul_greenwood · continued

36 tasks · 9 active · 27 completed

ACTIVE / NEEDS ATTENTION



lnr320

60s cut 7

Add text above both doors — needs rendering · waiting for approval

NEW_BG — RENDERED · waiting for approval

ACTIVE / NEEDS ATTENTION



sho060

new shots

Comp · in progress

ACTIVE / NEEDS ATTENTION



tvc020

TrainVsCar

bg env — needs comping · waiting for approval

COMPLETED



lnr170

60s cut 7

split plate [hidden task] · done

kill train [hidden task] · done

remove 3/4 signs · done

red square · done

sky love · done

paul_greenwood · continued

36 tasks · 9 active · 27 completed

COMPLETED · HIDDEN SHOT



lnr180

60s cut 7

puppet roto · done

COMPLETED



lnr190

60s cut 7

BG env — v03 · done

station/platform leaving [hidden task] · done

COMPLETED



lnr210

60s cut 7

bg env — v03 · done

COMPLETED



lnr230

60s cut 7

bg env — v04 · done

NEW_BG — RENDERERD · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

paul_greenwood · continued

36 tasks · 9 active · 27 completed

COMPLETED



lnr250

60s cut 7

bg env — v04 · done

Add Sign Above Door — Needs Rendering · done

NEW_BG — RENDERED · done

COMPLETED · HIDDEN SHOT



lnr260

60s cut 7

glass and reflection: — render and layout · done

COMPLETED



lnr280

60s cut 7

bg env — v06 [hidden task] · done

COMPLETED



lnr290

60s cut 7

bg env — v3 [hidden task] · done

paul_greenwood · continued

36 tasks · 9 active · 27 completed

COMPLETED



lnr320

60s cut 7

bg env_forward — v04
forward_direction · done

bg_env_backward — v001
Backward · done

pdf doors — needs rendering · done

COMPLETED



lnr330

60s cut 7

bg env — v004_FORWARD [hidden task] · done

COMPLETED



tip020

Tips

BG — RENDERED [hidden task] · done

BG_REVERSE · approved

COMPLETED



tip040

Tips

CG Background · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

paul_greenwood · continued

36 tasks · 9 active · 27 completed

COMPLETED



tip050

Tips

CG Background · done

COMPLETED



tip090

Tips

BG_RE_RENDER — ADDED MORE TREES · done

COMPLETED



tip150

Tips

CG Background · done

Prateek

74 tasks · 9 active · 65 completed

ACTIVE / NEEDS ATTENTION



lnr250

60s cut 7

hair [hidden task] · waiting for approval

ACTIVE / NEEDS ATTENTION



lnr270

60s cut 7

hair edge — stretch hair edge · waiting for approval

ACTIVE / NEEDS ATTENTION



lnr280

60s cut 7

Sky Color Fix · assigned

ACTIVE / NEEDS ATTENTION



lnr330

60s cut 7

removing wrinkles · waiting for approval

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Prateek · continued

74 tasks · 9 active · 65 completed

ACTIVE / NEEDS ATTENTION



lnr340

60s cut 7

Cleanup the fire · waiting for approval

ACTIVE / NEEDS ATTENTION



sho020

new shots

Comp — flickery · waiting for approval

ACTIVE / NEEDS ATTENTION



sho050

new shots

Comp · in progress

ACTIVE / NEEDS ATTENTION



spd010

SpendTheDayWithMe

Comp [hidden task] · in progress

Prateek · continued

74 tasks · 9 active · 65 completed

ACTIVE / NEEDS ATTENTION



tip120

Tips

Comp · waiting for approval

COMPLETED



con010

EleanorCore

Split plate · done

COMPLETED



con020

EleanorCore

Phone Screne tracking · done

COMPLETED



con030

EleanorCore

Comp · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Prateek · continued

74 tasks · 9 active · 65 completed

COMPLETED



con040

EleanorCore

Comp · done

COMPLETED



con050

EleanorCore

Comp · done

COMPLETED



con060

EleanorCore

Comp · done

COMPLETED



con070

EleanorCore

Comp · done

Prateek · continued

74 tasks · 9 active · 65 completed

COMPLETED



con080

EleanorCore

Comp · approved

COMPLETED



con090

EleanorCore

Comp · done

COMPLETED



con100

EleanorCore

Keying, roto & Comp · done

COMPLETED



con110

EleanorCore

Comp · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Prateek · continued

74 tasks · 9 active · 65 completed

COMPLETED



con120

EleanorCore

Comp · done

COMPLETED



con130

EleanorCore

Keying, roto & Comp · done

COMPLETED



lnr010

60s cut 7

extend range [hidden task] · done

COMPLETED



lnr070

60s cut 7

clean up roto · done

car badges and number plates · done

Prateek · continued

74 tasks · 9 active · 65 completed

COMPLETED



lnr090

60s cut 7

roto · done

split plate · done

logo removal · done

COMPLETED




lnr110

60s cut 7

wipe [hidden task] · done

hair white [hidden task] · done

COMPLETED · HIDDEN SHOT



lnr120

60s cut 7

whip transition · done

COMPLETED



lnr140

60s cut 7

Halo on hair [hidden task] · done

jimmys arm [hidden task] · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Prateek · continued

74 tasks · 9 active · 65 completed

COMPLETED



lnr150

60s cut 7

check mask on back of neck [hidden task] · done

COMPLETED



lnr160

60s cut 7

puppet roto [hidden task] · done

cow comp [hidden task] · done

shadow comp [hidden task] · done

build out back of bomber jacket [hidden task] · done

hair [hidden task] · done

COMPLETED · HIDDEN SHOT




lnr180

60s cut 7

split plate · done

COMPLETED



lnr200

60s cut 7

puppet roto · done

tracking marker paint · done

cg carriage · done

Remove rod · done

fix comp · done

Prateek · continued

74 tasks · 9 active · 65 completed

COMPLETED



lnr210

60s cut 7

kaleidoscope lens · done

Split plate — woman alt shot · done

remove LNER sticker from kaleidoscope · done

COMPLETED



lnr230

60s cut 7

remove marcs cracks · done

COMPLETED



lnr240

60s cut 7

puppet rod clean up · done

COMPLETED



lnr250

60s cut 7

Red line floor paint [hidden task] · done

add sign [hidden task] · done

Rod paint [hidden task] · done

removing wrinkles · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Prateek · continued

74 tasks · 9 active · 65 completed

COMPLETED · HIDDEN SHOT



lnr260

60s cut 7

model window · done

COMPLETED



lnr290

60s cut 7

removing wrinkles · done

Sky Color Fix · done

sign · done

COMPLETED



lnr310

60s cut 7

denoise [hidden task] · done

rod clean up [hidden task] · done

screen [hidden task] · done

move thumbs [hidden task] · done

8 bit game animation [hidden task] · done

COMPLETED



lnr330

60s cut 7

cg carriage [hidden task] · done

Prateek · continued

74 tasks · 9 active · 65 completed

COMPLETED



sho010

new shots

Comp · done

COMPLETED



sho030

new shots

Comp · done

COMPLETED



sho040

new shots

Comp · done

COMPLETED



tip020

Tips

Comp [hidden task] · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Prateek · continued

74 tasks · 9 active · 65 completed

COMPLETED



tip040

Tips

Comp · done

COMPLETED



tip050

Tips

Comp · done

COMPLETED



tip080

Tips

Comp · done

COMPLETED



tip090

Tips

Comp · done

Prateek · continued

74 tasks · 9 active · 65 completed

COMPLETED



tip140

Tips

Comp · done

COMPLETED



tip150

Tips

Comp · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Unassigned

60 tasks · 22 active · 38 completed

ACTIVE / NEEDS ATTENTION



cat010

CatchingUp

Rod paint · rejected

ACTIVE / NEEDS ATTENTION · HIDDEN SHOT



lnr030

60s cut 7

car camera paint — test · unassigned

ACTIVE / NEEDS ATTENTION



lnr070

60s cut 7

Sky replacement · unassigned

ACTIVE / NEEDS ATTENTION · HIDDEN SHOT



lnr130

60s cut 7

sky · unassigned

Unassigned · continued

60 tasks · 22 active · 38 completed

ACTIVE / NEEDS ATTENTION



lnr190

60s cut 7

Add text to sign above door — Needs Rendering [hidden task] · waiting for approval

sign · unassigned

ACTIVE / NEEDS ATTENTION



lnr290

60s cut 7

Red stripe floor paint · not started

ACTIVE / NEEDS ATTENTION



lnr300

60s cut 7

split plate — dad · unassigned

rod paint out · unassigned

ACTIVE / NEEDS ATTENTION



lnr320

60s cut 7

puppet roto · unassigned

sign · unassigned

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Unassigned · continued

60 tasks · 22 active · 38 completed

ACTIVE / NEEDS ATTENTION



lnr330

60s cut 7

sign · unassigned

ACTIVE / NEEDS ATTENTION



sho060

new shots

Match move — magic pie · unassigned

Roto · unassigned

ACTIVE / NEEDS ATTENTION



sho070

new shots

sign · unassigned

ACTIVE / NEEDS ATTENTION



sho080

new shots

sign · unassigned

Unassigned · continued

60 tasks · 22 active · 38 completed

ACTIVE / NEEDS ATTENTION



spo090

Spotting

Rod paint · rejected

bg · unassigned

ACTIVE / NEEDS ATTENTION



tip010

Tips

maybe tracked · unassigned

ACTIVE / NEEDS ATTENTION



tip100

Tips

Back carriage · unassigned

match still · unassigned

ACTIVE / NEEDS ATTENTION



tip160

Tips

Match move · unassigned


Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Unassigned · continued

60 tasks · 22 active · 38 completed

COMPLETED



cat020

CatchingUp

Rod paint · approved

COMPLETED




cat030

CatchingUp

Rod paint · approved

COMPLETED



cat040

CatchingUp

Rod paint · approved

COMPLETED



cat050

CatchingUp

rodpaint — matte line · approved

Unassigned · continued

60 tasks · 22 active · 38 completed

COMPLETED



cat060

CatchingUp

Rod paint · approved

COMPLETED



cat070

CatchingUp

Rod paint · approved

COMPLETED



cat080

CatchingUp

Rod paint · done

COMPLETED



cat090

CatchingUp

Rod paint · approved

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Unassigned · continued

60 tasks · 22 active · 38 completed

COMPLETED



lnr010

60s cut 7

new trees [hidden task] · done

COMPLETED



lnr100

60s cut 7

puppet roto · done

rod paint · done

roto of split plate on left · done

Rod shadow · done

COMPLETED



lnr110

60s cut 7

paint blue [hidden task] · done

COMPLETED



lnr160

60s cut 7

split plate [hidden task] · done

rod paint [hidden task] · done

Unassigned · continued

60 tasks · 22 active · 38 completed

COMPLETED



lnr190

60s cut 7

carpet [hidden task] · done

set up comp [hidden task] · done


paint out april · done

adjust train acceleration [hidden task] · done

Green screen in last few frames · done

key issue · done

COMPLETED



lnr200

60s cut 7

hair edge · done

COMPLETED



lnr210

60s cut 7

set up comp · done

COMPLETED



lnr220

60s cut 7

kscope fx · done

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Unassigned · continued

60 tasks · 22 active · 38 completed

COMPLETED



lnr250

60s cut 7

signs/lights [hidden task] · done

COMPLETED



lnr270

60s cut 7

cg carriage [hidden task] · done

set up comp [hidden task] · done

COMPLETED



lnr280

60s cut 7

Remove marker [hidden task] · done

COMPLETED



lnr290

60s cut 7

cg carriage [hidden task] · done

reverse shot of dad [hidden task] · done

Unassigned · continued

60 tasks · 22 active · 38 completed

COMPLETED



lnr310

60s cut 7

Skin tones? [hidden task] · done

COMPLETED



lnr320

60s cut 7

match move · done

COMPLETED



lnr330

60s cut 7

match move [hidden task] · done

Text above door [hidden task] · done

Move LNER logo around on cup [hidden task] · done

COMPLETED



spo080

Spotting

Rod paint · approved

Artist workboard · continued

Current tasks grouped by artist, then by active or completed work. A shared shot appears under each assigned artist.

Unassigned · continued

60 tasks · 22 active · 38 completed

COMPLETED



tip030


Tips

maybe tracked · done


Activity overview

Charts count recorded changes, not working hours or effort. All timelines and hidden shots are included.

Production events by week

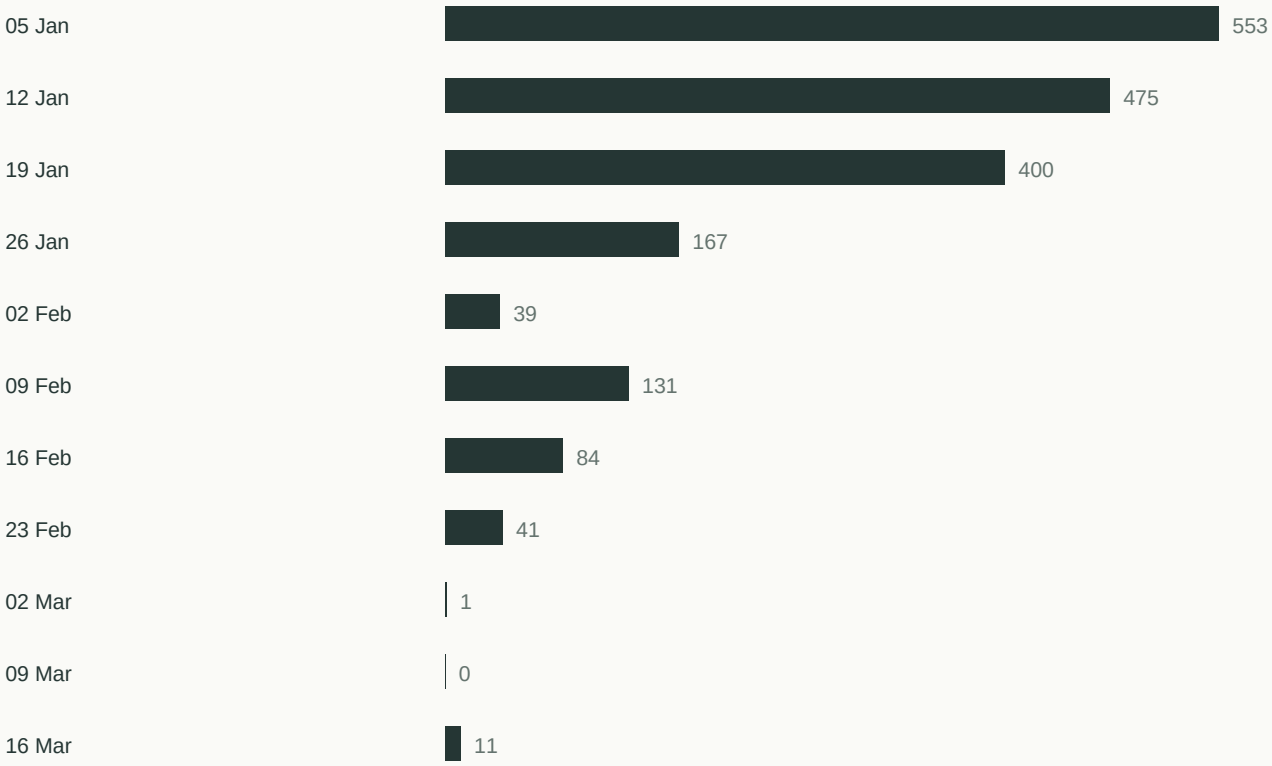

Where activity happened

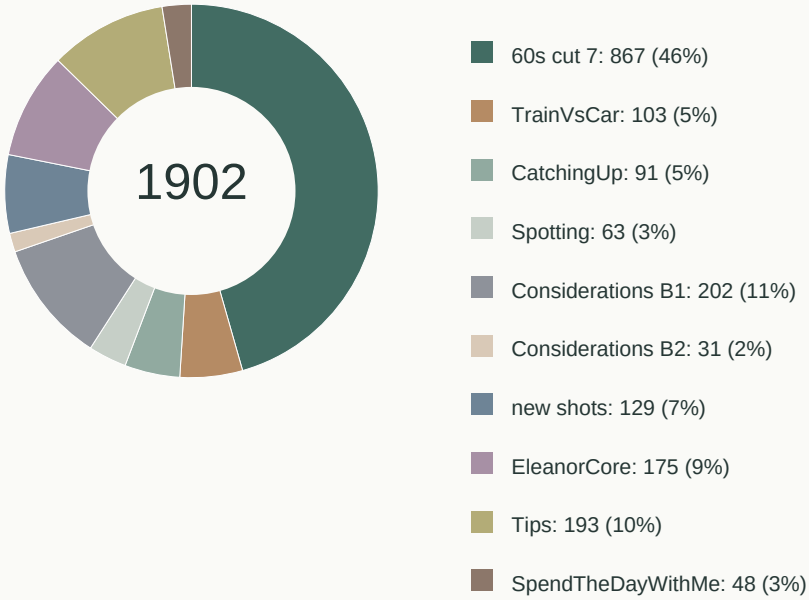

Shots with the most recorded changes



Included: task creation/deletion, assignments, status changes, conform and render updates. Excluded from charts: notes, colour, duration, shot creation and visibility edits. A conform update is not necessarily a new render or client revision.

Production rhythm


Daily activity, approval milestones and the mix of recorded changes.

Production activity calendar

	Mon	Tue	Wed	Thu	Fri	Sat	Sun
05 Jan	104	144	117	74	114	0	0
12 Jan	130	93	94	84	74	0	0
19 Jan	105	60	117	78	40	0	0
26 Jan	67	14	36	16	34	0	0
02 Feb	12	0	0	27	0	0	0
09 Feb	1	34	22	25	49	0	0
16 Feb	24	29	14	17	0	0	0
23 Feb	6	11	16	8	0	0	0
02 Mar	0	0	1	0	0	0	0
09 Mar	0	0	0	0	0	0	0
16 Mar	10	0	0	0	1	–	–


Cell values are event counts. Darker cells mean more recorded changes; zero means no logged production events.

Cumulative approval / completion events

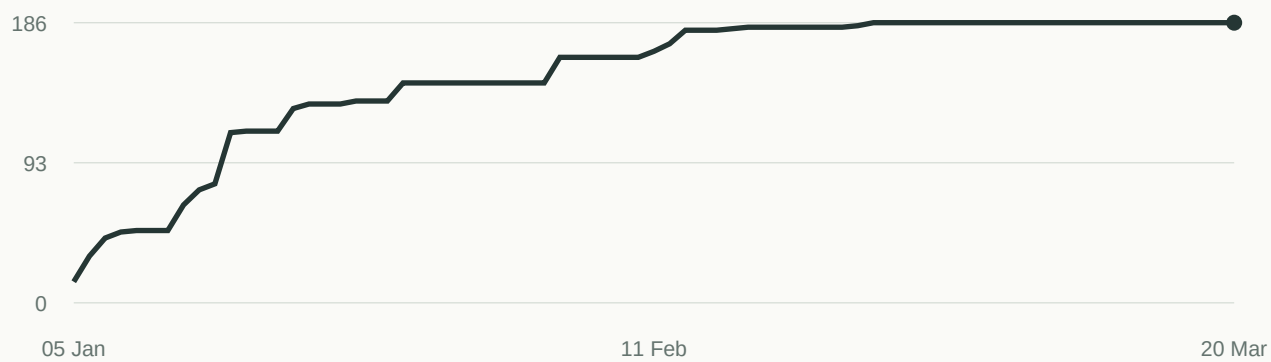


Historical transitions into Approved or Done, including repeated approvals and deleted tasks. This is not the count of currently completed tasks.

Production event mix

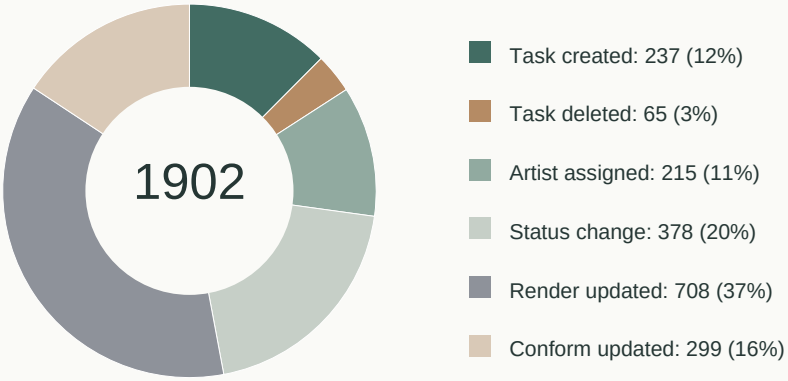

People & record quality

Recorded actions by author

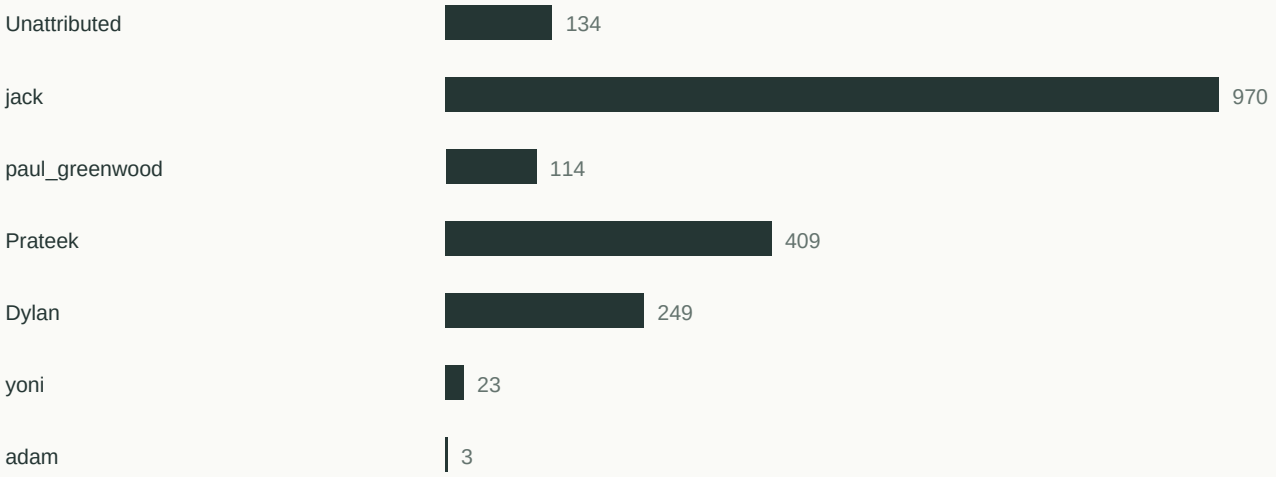

Current task assignments

Artist	Assigned tasks	Approved / done
Dylan	21	3
Joe	10	8
Prateek	74	65
Unassigned	60	38
adam	8	7
cronk	3	1
jack	59	43
outsource	1	1
paul_greenwood	36	27

Approval record

10 tasks approved; 183 tasks done; 22 tasks awaiting approval; 57 tasks in other open states.

Outstanding: lnr040 — roto face (cronk, in progress); lnr030 — car camera paint (Unassigned, unassigned); lnr130 — sky (Unassigned, unassigned); lnr170 — puppet roto (Joe, waiting for approval); lnr300 — bg env (paul_greenwood, rejected); lnr300 — split plate (Unassigned, unassigned); lnr320 — puppet roto (Unassigned, unassigned); tvc020 — greenscreen (Dylan, waiting for approval); tvc040 — paint (Dylan, waiting for approval); tvc060 — paint (Dylan, waiting for approval); lnr020 — painting (cronk, unassigned); lnr020 — test (Dylan, assigned); lnr270 — hair edge (Prateek, waiting for approval); cat010 — Rod paint (Unassigned, rejected); spo090 — Rod paint (Unassigned, rejected); spo120 — Match move (jack, unassigned); cnb010 — Match move (jack, unassigned); cnb030 — Match move (jack, unassigned); cnb040 — Match move (jack, unassigned); cnb050 — Match move (jack, unassigned); tvc020 — bg env (paul_greenwood, waiting for approval); cat010 — bg env (paul_greenwood, unassigned); tvc080 — Paint (Dylan, waiting for approval); tvc100 — Paint (Dylan, waiting for approval); tvc100 — Paint (Dylan, waiting for approval); tvc080 — Paint (Dylan, waiting for approval); lnr300 — rod paint out (Unassigned, unassigned); cat010 — Comp (jack, unassigned); cat020 — Comp (jack, unassigned); cat030 — Comp (jack, unassigned); cat040 — Comp (jack, unassigned); tvc120 — Paint (Dylan, waiting for approval); tvc140 — Paint (Dylan, in progress); tvc160 — Paint (Dylan, in progress); tvc180 — Paint (Dylan, in

progress); spo040 — Comp (Dylan, unassigned); spo050 — Rod paint (Dylan, unassigned); spo060 — Rod paint (Dylan, unassigned); spo100 — carrage (Dylan, unassigned); spo120 — Comp (Dylan, unassigned); cna010 — Comp (adam, assigned); sho020 — Comp (Prateek, waiting for approval); sho050 — Comp (Prateek, in progress); sho060 — Match move (Unassigned, unassigned); sho070 — Roto (jack, unassigned); sho080 — Roto (jack, unassigned); lnr070 — Sky replacement (Unassigned, unassigned); lnr190 — Add text to sign above door (Unassigned, waiting for approval); lnr290 — Red stripe floor paint (Unassigned, not started); lnr320 — Add text above both doors (paul_greenwood, waiting for approval); spo080 — carrrage (Dylan, unassigned); spo090 — bg (Unassigned, unassigned); sho070 — Comp (jack, unassigned); sho080 — Comp (jack, unassigned); sho060 — Roto (Unassigned, unassigned); lnr170 — finish o (Joe, in progress); lnr290 — Add text above door (paul_greenwood, waiting for approval); lnr250 — hair (Prateek, waiting for approval); lnr170 — add lady (jack, not started); lnr010 — make plane bigger (jack, unassigned); lnr070 — remove people (jack, unassigned); sho060 — Comp (paul_greenwood, in progress); lnr330 — removing wrinkles (Prateek, waiting for approval); lnr340 — Cleanup the fire (Prateek, waiting for approval); lnr300 — NEW BG RENDER (paul_greenwood, waiting for approval); lnr320 — NEW_BG (paul_greenwood, waiting for approval); lnr280 — NEW BG BACKGROUND (paul_greenwood, waiting for approval); lnr280 — Sky Color Fix (Prateek, assigned); lnr190 — sign (Unassigned, unassigned); lnr320 — sign (Unassigned, unassigned); lnr330 — sign (Unassigned, unassigned); sho070 — sign (Unassigned, unassigned); sho080 — sign (Unassigned, unassigned); spd010 — Comp (Prateek, in progress); tip100 — Back carriage (Unassigned, unassigned); tip010 — maybe tracked (Unassigned, unassigned); tip100 — match still (Unassigned, unassigned); tip160 — Match move (Unassigned, unassigned); tip120 — Comp (Prateek, waiting for approval)

186 recorded transitions into Approved or Done. These are historical events, including repeated approvals and tasks subsequently deleted.

How to read this report

240 of 2531 total activity records have no recorded author. Assignment history names the assigned artist; it does not identify who performed an action. Neither chart is a productivity ranking.

Shot cards show current tasks and recorded historical assignments. Hidden tasks are labelled. Deleted tasks may still contribute activity but are absent from the current task list.


Activity spans run from the first to last recorded event on each shot and can include later administrative edits. They do not measure hours worked. No work-time estimates are made.

Task titles and notes are kept literal. Approval applies to individual tasks; a shot without tasks is not assumed approved. Latest conform filenames are recorded references, not verified delivery files.

60s cut 7

34 shots · 10 hidden · 867 production events

131 tasks done; 11 tasks awaiting approval; 19 tasks in other open states.



lnr010

Recorded work: “match move”, “set scan”, “prep 3d”, “new trees”, “extend range”, “fix roto”, “remove car branding”, “number plates”, “reduce density of trees” and “make plane bigger”.

Task / note	Assigned to	Status
match move [hidden]	jack	done
set scan — photo geo [hidden]	jack	done
prep 3d [hidden]	jack	done
new trees [hidden]	Unassigned	done
extend range [hidden]	Prateek	done
fix roto [hidden]	jack	done
remove car branding [hidden]	Joe	done
number plates [hidden]	Joe	done
reduce density of trees [hidden]	Joe	done
make plane bigger [hidden]	jack	unassigned

Historical assignments: Joe, Prateek, jack

Latest recorded approval / done: 15 Jan 2026

77 recorded events · 15 active dates
05 Jan – 26 Jan 2026 · 21 elapsed days

Latest conform: lnr010_v25.mov



lnr020 / HIDDEN

Recorded work: “painting”, “New Task” and “test”.

Task / note	Assigned to	Status
painting — paint the car	cronk	unassigned
New Task	cronk	done
test	Dylan	assigned

Historical assignments: Dylan, cronk

6 recorded events · 1 active date
05 Jan – 05 Jan 2026 · 0 elapsed days



lnr030 / HIDDEN

Recorded work: “car camera paint”.

Task / note	Assigned to	Status
car camera paint — test	Unassigned	unassigned

7 recorded events · 4 active dates
05 Jan – 13 Feb 2026 · 39 elapsed days




lnr040 / HIDDEN

Recorded work: “roto face”.

Task / note	Assigned to	Status
roto face	cronk	in progress

4 recorded events · 2 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days



lnr050 / HIDDEN

No task-level work description is recorded.



lnr060 / HIDDEN

No task-level work description is recorded.



lnr070

Recorded work: “clean up roto”, “car badges and number plates”, “Sky replacement” and “remove people”.

Task / note	Assigned to	Status
clean up roto	Prateek	done
car badges and number plates	Prateek	done
Sky replacement	Unassigned	unassigned
remove people	jack	unassigned

Historical assignments: Prateek, jack

Latest recorded approval / done: 19 Jan 2026

30 recorded events · 9 active dates
05 Jan – 21 Jan 2026 · 16 elapsed days

Latest conform: lnr070_v09.mov



lnr080 / HIDDEN

No task-level work description is recorded.



lnr090

Recorded work: “roto”, “split plate” and “logo removal”.

Task / note	Assigned to	Status
roto	Prateek	done
split plate	Prateek	done
logo removal	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 15 Jan 2026

14 recorded events · 6 active dates
05 Jan – 21 Jan 2026 · 16 elapsed days

Latest conform: lnr090_v09.mov



lnr100

Recorded work: “puppet roto”, “split plate”, “rod paint”, “Comp”, “car branding/number plate”, “roto of split plate on left” and “Rod shadow”.

Task / note	Assigned to	Status
puppet roto	Unassigned	done
split plate	jack	done
rod paint	Unassigned	done
Comp	jack	done
car branding/number plate	jack	done
roto of split plate on left	Unassigned	done
Rod shadow	Unassigned	done

Historical assignments: jack

Latest recorded approval / done: 07 Jan 2026

18 recorded events · 5 active dates
05 Jan – 21 Jan 2026 · 16 elapsed days

Latest conform: lnr100_v07.mov



lnr110

Recorded work: “puppet roto”, “wipe”, “paint blue” and “hair white”.


Task / note	Assigned to	Status
puppet roto [hidden]	jack	done
wipe [hidden]	Prateek	done
paint blue [hidden]	Unassigned	done
hair white [hidden]	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 13 Jan 2026

40 recorded events · 10 active dates
05 Jan – 21 Jan 2026 · 16 elapsed days

Latest conform: lnr110_v23.mov



lnr120 / HIDDEN

Recorded work: “whip transition”.

Task / note	Assigned to	Status
whip transition	Prateek	done

Latest recorded approval / done: 12 Jan 2026

2 recorded events · 1 active date
12 Jan – 12 Jan 2026 · 0 elapsed days



lnr130 / HIDDEN

Recorded work: “sky”.

Task / note	Assigned to	Status
sky	Unassigned	unassigned



lnr140

Recorded work: “refine comp”, “check eleanor roto”, “contact shadows for eleanor”, “eleanor sharpening”, “eleanor shadow on floor”, “Halo on hair” and “jimmys arm”.

Task / note	Assigned to	Status
refine comp [hidden]	Joe	done
check eleanor roto [hidden]	Joe	done
contact shadows for eleanor [hidden]	Joe	done
eleanor sharpening [hidden]	Joe	done
eleanor shadow on floor [hidden]	Joe	done
Halo on hair [hidden]	Prateek	done
jimmys arm [hidden]	Prateek	done

Historical assignments: Joe, Prateek

Latest recorded approval / done: 19 Jan 2026

51 recorded events · 11 active dates
05 Jan – 23 Jan 2026 · 18 elapsed days

Latest conform: lnr140_v19.mov



lnr150

Recorded work: “puppet roto” and “check mask on back of neck”.

Task / note	Assigned to	Status
puppet roto [hidden]	jack	done
check mask on back of neck [hidden]	Prateek	done

Historical assignments: Prateek, jack

Latest recorded approval / done: 19 Jan 2026

20 recorded events · 5 active dates
06 Jan – 19 Jan 2026 · 13 elapsed days

Latest conform: lnr150_v29.mov (MOV)



lnr160

Recorded work: “puppet roto”, “split plate”, “rod paint”, “cow comp”, “shadow comp”, “build out back of bomber jacket” and “hair”.

Task / note	Assigned to	Status
puppet roto [hidden]	Prateek	done
split plate [hidden]	Unassigned	done
rod paint [hidden]	Unassigned	done
cow comp [hidden]	Prateek	done
shadow comp [hidden]	Prateek	done
build out back of bomber jacket [hidden]	Prateek	done
hair [hidden]	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 19 Jan 2026

41 recorded events · 10 active dates
05 Jan – 27 Jan 2026 · 22 elapsed days

Latest conform: lnr160_v41_####.exr 1001-1087



lnr170

Recorded work: “puppet roto”, “split plate”, “kill train”, “remove 3/4 signs”, “red square”, “sky love”, “Roto”, “finish o” and “add lady”.

Task / note	Assigned to	Status
puppet roto — Harvey [hidden]	Joe	waiting for approval
split plate [hidden]	paul_greenwood	done
kill train [hidden]	paul_greenwood	done
remove 3/4 signs	paul_greenwood	done
red square	paul_greenwood	done
sky love	paul_greenwood	done
Roto	outsource	done
finish o	Joe	in progress
add lady — suitcase	jack	not started

Historical assignments: Joe, jack, outsource, paul_greenwood

Latest recorded approval / done: 15 Jan 2026

49 recorded events · 10 active dates
06 Jan – 23 Jan 2026 · 17 elapsed days

Latest conform: lnr170_v36_####.exr 1026-1088



lnr180 / HIDDEN

Recorded work: “puppet roto” and “split plate”.

Task / note	Assigned to	Status
puppet roto	paul_greenwood	done
split plate	Prateek	done

2 recorded events · 2 active dates
12 Jan – 14 Jan 2026 · 2 elapsed days

Latest conform: lnr180_v09.mov



lnr190

Recorded work: “train 3d”, “BG env”, “carpet”, “key”, “set up comp”, “paint out april”, “station/platform leaving”, “adjust train acceleration”, “Add text to sign above door”, “Green screen in last few frames”, “key issue” and “sign”.

Task / note	Assigned to	Status
train 3d [hidden]	jack	done
BG env — v03	paul_greenwood	done
carpet [hidden]	Unassigned	done
key [hidden]	jack	done
set up comp [hidden]	Unassigned	done
paint out april	Unassigned	done
station/platform leaving [hidden]	paul_greenwood	done
adjust train acceleration [hidden]	Unassigned	done
Add text to sign above door — Needs Rendering [hidden]	Unassigned	waiting for approval
Green screen in last few frames	Unassigned	done
key issue	Unassigned	done
sign	Unassigned	unassigned

Historical assignments: paul_greenwood

Latest recorded approval / done: 26 Jan 2026

58 recorded events · 12 active dates
06 Jan – 26 Jan 2026 · 20 elapsed days

Latest conform: lnr190_v36.mov



lnr200

Recorded work: “puppet roto”, “tracking marker paint”, “cg carriage”, “tilt background train”, “hair edge”, “Remove rod” and “fix comp”.

Task / note	Assigned to	Status
puppet roto	Prateek	done
tracking marker paint	Prateek	done
cg carriage	Prateek	done
tilt background train	jack	done
hair edge	Unassigned	done
Remove rod	Prateek	done
fix comp	Prateek	done

Historical assignments: Prateek, jack

Latest recorded approval / done: 26 Jan 2026

40 recorded events · 11 active dates
05 Jan – 26 Jan 2026 · 21 elapsed days

Latest conform: lnr200_v22.mov (MOV)



lnr210

Recorded work: “camera match”, “bg env”, “kaleidoscope lens”, “set up comp”, “Split plate” and “remove LNER sticker from kaleidoscope”.

Task / note	Assigned to	Status
camera match	jack	done
bg env — v03	paul_greenwood	done
kaleidoscope lens	Prateek	done
set up comp	Unassigned	done
Split plate — woman alt shot	Prateek	done
remove LNER sticker from kaleidoscope	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 12 Jan 2026

24 recorded events · 6 active dates
05 Jan – 22 Jan 2026 · 17 elapsed days

Latest conform: lnr210_v09.mov



lnr220

Recorded work: “camera match”, “cg carriage”, “puppet roto”, “rod paint” and “kscope fx”.

Task / note	Assigned to	Status
camera match	jack	done
cg carriage	jack	done
puppet roto	jack	done
rod paint	jack	done
kscope fx	Unassigned	done

Historical assignments: jack

Latest recorded approval / done: 07 Jan 2026

9 recorded events · 4 active dates
05 Jan – 14 Jan 2026 · 9 elapsed days

Latest conform: lnr220_v15.mov



lnr230

Recorded work: “remove apple logo”, “remove marcs cracks”, “bg env” and “NEW_BG”.

Task / note	Assigned to	Status
remove apple logo [hidden]	Dylan	done
remove marcs cracks	Prateek	done
bg env — v04	paul_greenwood	done
NEW_BG — RENDERERD	paul_greenwood	done

Historical assignments: Dylan, Prateek, jack, paul_greenwood

Latest recorded approval / done: 26 Jan 2026

38 recorded events · 10 active dates
05 Jan – 26 Jan 2026 · 21 elapsed days

Latest conform: lnr230_v18_####.exr 1001-1089



lnr240

Recorded work: “puppet rod clean up”.

Task / note	Assigned to	Status
puppet rod clean up	Prateek	done

Latest recorded approval / done: 05 Jan 2026

5 recorded events · 2 active dates
05 Jan – 06 Jan 2026 · 1 elapsed day

Latest conform: lnr240_v05.mov



lnr250

Recorded work: “camera match”, “bg env”, “remove cup”, “split”, “set up comp”, “signs/lights”, “Red line floor paint”, “Add Sign Above Door”, “hair”, “add sign”, “Rod paint”, “removing wrinkles”, “NEW_BG” and “sign”.

Task / note	Assigned to	Status
camera match [hidden]	jack	done
bg env — v04	paul_greenwood	done
remove cup [hidden]	jack	done
split [hidden]	jack	done
set up comp [hidden]	jack	done
signs/lights [hidden]	Unassigned	done
Red line floor paint [hidden]	Prateek	done
Add Sign Above Door — Needs Rendering	paul_greenwood	done
hair [hidden]	Prateek	waiting for approval
add sign [hidden]	Prateek	done
Rod paint [hidden]	Prateek	done
removing wrinkles	Prateek	done
NEW_BG — RENDERED	paul_greenwood	done
sign	Dylan	done

Historical assignments: Dylan, Prateek, jack, paul_greenwood

Latest recorded approval / done: 26 Jan 2026

104 recorded events · 14 active dates
05 Jan – 26 Jan 2026 · 21 elapsed days

Latest conform: lnr250_v41_####.exr 1001-1116



lnr260 / HIDDEN

Recorded work: “glass and reflection:” and “model window”.

Task / note	Assigned to	Status
glass and reflection: — render and layout	paul_greenwood	done
model window	Prateek	done

Historical assignments: Prateek, paul_greenwood

Latest recorded approval / done: 15 Jan 2026

15 recorded events · 4 active dates
06 Jan – 15 Jan 2026 · 9 elapsed days

Latest conform: lnr260_v03.mov



lnr270

Recorded work: “camera match”, “cg carriage”, “set up comp” and “hair edge”.

Task / note	Assigned to	Status
camera match [hidden]	jack	done
cg carriage [hidden]	Unassigned	done
set up comp [hidden]	Unassigned	done
hair edge — stretch hair edge	Prateek	waiting for approval

Historical assignments: Joe, Prateek, jack

Latest recorded approval / done: 05 Jan 2026

43 recorded events · 11 active dates
05 Jan – 22 Jan 2026 · 17 elapsed days

Latest conform: lnr270_v29_####.exr 1001-1075



lnr280

Recorded work: “match move”, “bg env”, “Remove marker”, “make field nicer”, “NEW BG BACKGROUND” and “Sky Color Fix”.

Task / note	Assigned to	Status
match move [hidden]	jack	done
bg env — v06 [hidden]	paul_greenwood	done
Remove marker [hidden]	Unassigned	done
make field nicer [hidden]	jack	done
NEW BG BACKGROUND — RENDERED	paul_greenwood	waiting for approval
Sky Color Fix	Prateek	assigned

Historical assignments: Prateek, jack, paul_greenwood

Latest recorded approval / done: 19 Jan 2026

55 recorded events · 8 active dates
12 Jan – 26 Jan 2026 · 14 elapsed days

Latest conform: lnr280_v44_####.exr 1020-1099



lnr290

Recorded work: “bg env”, “cg carriage”, “rod clean up”, “splits”, “reverse shot of dad”, “Red stripe floor paint”, “Add text above door”, “removing wrinkles”, “Sky Color Fix” and “sign”.

Task / note	Assigned to	Status
bg env — v3 [hidden]	paul_greenwood	done
cg carriage [hidden]	Unassigned	done
rod clean up [hidden]	jack	done
splits — reverce dad [hidden]	jack	done
reverse shot of dad [hidden]	Unassigned	done
Red stripe floor paint	Unassigned	not started
Add text above door — Need Rendering	paul_greenwood	waiting for approval
removing wrinkles	Prateek	done
Sky Color Fix	Prateek	done
sign	Prateek	done

Historical assignments: Joe, Prateek, jack, paul_greenwood

Latest recorded approval / done: 26 Jan 2026

82 recorded events · 13 active dates
05 Jan – 26 Jan 2026 · 21 elapsed days

Latest conform: lnr290_v36_####.exr 1001-1088



lnr300

Recorded work: “bg env”, “split plate”, “rod paint out” and “NEW BG RENDER”.

Task / note	Assigned to	Status
bg env — v03 reverse	paul_greenwood	rejected
split plate — dad	Unassigned	unassigned
rod paint out	Unassigned	unassigned
NEW BG RENDER — RENDERERD	paul_greenwood	waiting for approval

Historical assignments: Prateek, paul_greenwood

41 recorded events · 8 active dates
05 Jan – 23 Jan 2026 · 18 elapsed days

Latest conform: lnr300_v25_####.exr 1025-1052



lnr310

Recorded work: “denoise”, “rod clean up”, “screen”, “move thumbs”, “8 bit game animation” and “Skin tones?”.

Task / note	Assigned to	Status
denoise [hidden]	Prateek	done
rod clean up [hidden]	Prateek	done
screen [hidden]	Prateek	done
move thumbs [hidden]	Prateek	done
8 bit game animation [hidden]	Prateek	done
Skin tones? [hidden]	Unassigned	done

Historical assignments: Prateek

Latest recorded approval / done: 13 Jan 2026

48 recorded events · 9 active dates
06 Jan – 20 Jan 2026 · 14 elapsed days

Latest conform: lnr310_v16_####.exr (EXR)



lnr320

Recorded work: “match move”, “puppet roto”, “cg carriage”, “bg env_forward”, “bg_env_backward”, “Add text above both doors”, “pdf doors”, “NEW_BG” and “sign”.


Task / note	Assigned to	Status
match move	Unassigned	done
puppet roto	Unassigned	unassigned
cg carriage — NEEDED FOR BOTH ENDS	jack	done
bg env_forward — v04 forward_direction	paul_greenwood	done
bg_env_backward — v001 Backward	paul_greenwood	done
Add text above both doors — needs rendering	paul_greenwood	waiting for approval
pdf doors — needs rendering	paul_greenwood	done
NEW_BG — RENDERED	paul_greenwood	waiting for approval
sign	Unassigned	unassigned

Historical assignments: jack, paul_greenwood

Latest recorded approval / done: 26 Jan 2026

78 recorded events · 13 active dates
06 Jan – 26 Jan 2026 · 20 elapsed days

Latest conform: lnr320_v38_####.exr 1001-1135



lnr330

Recorded work: “match move”, “cg carriage”, “bg env”, “keying issue”, “Text above door”, “Move LNER logo around on cup”, “removing wrinkles” and “sign”.

Task / note	Assigned to	Status
match move [hidden]	Unassigned	done
cg carriage [hidden]	Prateek	done
bg env — v004_FORWARD [hidden]	paul_greenwood	done
keying issue [hidden]	jack	done
Text above door [hidden]	Unassigned	done
Move LNER logo around on cup [hidden]	Unassigned	done
removing wrinkles	Prateek	waiting for approval
sign	Unassigned	unassigned

Historical assignments: Prateek, jack, paul_greenwood

Latest recorded approval / done: 15 Jan 2026

60 recorded events · 12 active dates
07 Jan – 26 Jan 2026 · 19 elapsed days

Latest conform: lnr330_v20_####.exr 1001-1130



lnr340

Recorded work: “Cleanup the fire”.

Task / note	Assigned to	Status
Cleanup the fire	Prateek	waiting for approval

Historical assignments: Prateek

7 recorded events · 3 active dates
21 Jan – 23 Jan 2026 · 2 elapsed days

Latest conform: lnr340_v04.mov

TrainVsCar

18 shots · 9 hidden · 103 production events

2 tasks done; 9 tasks awaiting approval; 3 tasks in other open states.



tvc010 / HIDDEN

No task-level work description is recorded.

1 recorded events · 1 active date
06 Jan – 06 Jan 2026 · 0 elapsed days



tvc020

Recorded work: “match camera”, “greenscreen”, “bg env” and “Roto”.

Task / note	Assigned to	Status
match camera	jack	done
greenscreen	Dylan	waiting for approval
bg env — needs comping	paul_greenwood	waiting for approval
Roto — fix cam stab	Dylan	done

Historical assignments: Dylan, jack, paul_greenwood

Latest recorded approval / done: 07 Jan 2026

27 recorded events · 7 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days

Latest conform: tvc020_v10.mov



tvc030 / HIDDEN

No task-level work description is recorded.

1 recorded events · 1 active date
06 Jan – 06 Jan 2026 · 0 elapsed days



tvc040

Recorded work: “paint”.

Task / note	Assigned to	Status
paint	Dylan	waiting for approval

8 recorded events · 4 active dates
07 Jan – 13 Jan 2026 · 6 elapsed days

Latest conform: tvc040_v03.mov



tvc050 / HIDDEN

No task-level work description is recorded.

1 recorded events · 1 active date
06 Jan – 06 Jan 2026 · 0 elapsed days



tvc060

Recorded work: “paint”.

Task / note	Assigned to	Status
paint	Dylan	waiting for approval

6 recorded events · 4 active dates
07 Jan – 13 Jan 2026 · 6 elapsed days

Latest conform: tvc060_v02.mov



tvc070 / HIDDEN

No task-level work description is recorded.



tvc080

Recorded work: “Paint”.

Task / note	Assigned to	Status
Paint	Dylan	waiting for approval
Paint — fix roto	Dylan	waiting for approval

Historical assignments: Dylan

15 recorded events · 5 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days

Latest conform: tvc080_v03.mov



tvc090 / HIDDEN

No task-level work description is recorded.



tvc100

Recorded work: “Paint”.

Task / note	Assigned to	Status
Paint	Dylan	waiting for approval
Paint — fix ro	Dylan	waiting for approval

Historical assignments: Dylan

15 recorded events · 5 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days

Latest conform: tvc100_v02.mov



tvc110 / HIDDEN

No task-level work description is recorded.



tvc120

Recorded work: “Paint”.

Task / note	Assigned to	Status
Paint	Dylan	waiting for approval

Historical assignments: Dylan

12 recorded events · 6 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days

Latest conform: tvc120_v03.mov



tvc130 / HIDDEN

No task-level work description is recorded.



tvc140

Recorded work: “Paint”.

Task / note	Assigned to	Status
Paint	Dylan	in progress

Historical assignments: Dylan

10 recorded events · 5 active dates
08 Jan – 20 Jan 2026 · 12 elapsed days

Latest conform: tvc140_v08.mov



tvc150 / HIDDEN

No task-level work description is recorded.



tvc160

Recorded work: “Paint”.

Task / note	Assigned to	Status
Paint	Dylan	in progress

Historical assignments: Dylan

11 recorded events · 4 active dates
08 Jan – 20 Jan 2026 · 12 elapsed days

Latest conform: tvc160_v04.mov



tvc170 / HIDDEN

No task-level work description is recorded.



tvc180

Recorded work: “Paint”.

Task / note	Assigned to	Status
Paint	Dylan	in progress

Historical assignments: Dylan

10 recorded events · 4 active dates
08 Jan – 19 Jan 2026 · 11 elapsed days

Latest conform: tvc180_v03.mov

CatchingUp

9 shots · 0 hidden · 91 production events

7 tasks approved; 2 tasks done; 6 tasks in other open states.



cat010

Recorded work: “Rod paint”, “Camera match”, “bg env” and “Comp”.


Task / note	Assigned to	Status
Rod paint	Unassigned	rejected
Camera match	jack	done
bg env	paul_greenwood	unassigned
Comp	jack	unassigned

Historical assignments: jack, paul_greenwood

Latest recorded approval / done: 05 Jan 2026

25 recorded events · 7 active dates
05 Jan – 19 Jan 2026 · 14 elapsed days

Latest conform: cat010_v10.mov



cat020

Recorded work: “Rod paint” and “Comp”.


Task / note	Assigned to	Status
Rod paint	Unassigned	approved
Comp	jack	unassigned

Historical assignments: jack

Latest recorded approval / done: 06 Jan 2026

13 recorded events · 6 active dates
05 Jan – 19 Jan 2026 · 14 elapsed days

Latest conform: cat020_v04.mov



cat030

Recorded work: “Rod paint” and “Comp”.

Task / note	Assigned to	Status
Rod paint	Unassigned	approved
Comp	jack	unassigned

Historical assignments: jack

Latest recorded approval / done: 06 Jan 2026

12 recorded events · 6 active dates
05 Jan – 19 Jan 2026 · 14 elapsed days

Latest conform: cat030_v04.mov



cat040


Recorded work: “Rod paint” and “Comp”.

Task / note	Assigned to	Status
Rod paint	Unassigned	approved
Comp	jack	unassigned

Historical assignments: jack

Latest recorded approval / done: 05 Jan 2026

10 recorded events · 4 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days




cat050

Recorded work: “rodpaint”.

Task / note	Assigned to	Status
rodpaint — matte line	Unassigned	approved

Latest recorded approval / done: 06 Jan 2026

8 recorded events · 4 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days




cat060

Recorded work: “Rod paint”.

Task / note	Assigned to	Status
Rod paint	Unassigned	approved

Latest recorded approval / done: 05 Jan 2026

5 recorded events · 3 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days




cat070

Recorded work: “Rod paint”.

Task / note	Assigned to	Status
Rod paint	Unassigned	approved

Latest recorded approval / done: 05 Jan 2026

8 recorded events · 3 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days



cat080

Recorded work: “Rod paint”.

Task / note	Assigned to	Status
Rod paint	Unassigned	done

Latest recorded approval / done: 06 Jan 2026

9 recorded events · 4 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days



cat090

Recorded work: “Rod paint”.

Task / note	Assigned to	Status
Rod paint	Unassigned	approved

Latest recorded approval / done: 06 Jan 2026

8 recorded events · 4 active dates
05 Jan – 13 Jan 2026 · 8 elapsed days

Spotting

12 shots · 3 hidden · 63 production events


1 task approved; 4 tasks done; 9 tasks in other open states.



spo010 / HIDDEN

No task-level work description is recorded.

5 recorded events · 3 active dates
08 Jan – 23 Jan 2026 · 15 elapsed days



spo020 / HIDDEN

No task-level work description is recorded.


1 recorded events · 1 active date
08 Jan – 08 Jan 2026 · 0 elapsed days



spo030 / HIDDEN

No task-level work description is recorded.

1 recorded events · 1 active date
08 Jan – 08 Jan 2026 · 0 elapsed days



spo040

Recorded work: “Camera match” and “Comp”.


Task / note	Assigned to	Status
Camera match	jack	done
Comp	Dylan	unassigned

Historical assignments: Dylan, jack

Latest recorded approval / done: 05 Jan 2026

10 recorded events · 5 active dates
05 Jan – 14 Jan 2026 · 9 elapsed days

Latest conform: spo040_v02.mov



spo050


Recorded work: “Rod paint”.

Task / note	Assigned to	Status
Rod paint	Dylan	unassigned

Historical assignments: Dylan

4 recorded events · 3 active dates
09 Jan – 13 Jan 2026 · 4 elapsed days

Latest conform: spo050_v02.mov



spo060

Recorded work: “Rod paint”.

Task / note	Assigned to	Status
Rod paint	Dylan	unassigned

Historical assignments: Dylan

4 recorded events · 3 active dates
09 Jan – 13 Jan 2026 · 4 elapsed days

Latest conform: spo060_v02.mov




spo070

No task-level work description is recorded.

2 recorded events · 2 active dates
12 Jan – 13 Jan 2026 · 1 elapsed day

Latest conform: spo070_v02.mov



spo080

Recorded work: “Rod paint”, “Match move” and “carrrage”.

Task / note	Assigned to	Status
Rod paint	Unassigned	approved
Match move	jack	done
carrrage	Dylan	unassigned

Historical assignments: Dylan, jack

Latest recorded approval / done: 06 Jan 2026

13 recorded events · 5 active dates
05 Jan – 14 Jan 2026 · 9 elapsed days

Latest conform: spo080_v04.mov



spo090


Recorded work: “Rod paint”, “Camera match” and “bg”.

Task / note	Assigned to	Status
Rod paint	Unassigned	rejected
Camera match	jack	done
bg	Unassigned	unassigned

Historical assignments: jack

Latest recorded approval / done: 06 Jan 2026

12 recorded events · 5 active dates
05 Jan – 14 Jan 2026 · 9 elapsed days



spo100

Recorded work: “Match move” and “carrage”.

Task / note	Assigned to	Status
Match move	jack	done
carrage	Dylan	unassigned

Historical assignments: Dylan, jack

Latest recorded approval / done: 06 Jan 2026


12 recorded events · 8 active dates
05 Jan – 22 Jan 2026 · 17 elapsed days

Latest conform: spo100_v02.mov



spo110

No task-level work description is recorded.



spo120

Recorded work: “Match move” and “Comp”.

Task / note	Assigned to	Status
Match move — dont need match move use other plate	jack	unassigned
Comp	Dylan	unassigned

Historical assignments: Dylan, jack

9 recorded events · 4 active dates
05 Jan – 14 Jan 2026 · 9 elapsed days

Latest conform: spo120_v02.mov

Considerations B1

7 shots · 1 hidden · 202 production events

5 tasks done; 1 task in other open states.



cna010

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	adam	assigned

Historical assignments: adam, jack

41 recorded events · 11 active dates
06 Jan – 23 Jan 2026 · 17 elapsed days

Latest conform: cna010_v07.mov



cna020 / HIDDEN

No task-level work description is recorded.

11 recorded events · 1 active date
06 Jan – 06 Jan 2026 · 0 elapsed days



cna030

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	adam	done

Historical assignments: adam, jack

Latest recorded approval / done: 19 Jan 2026

25 recorded events · 9 active dates
06 Jan – 22 Jan 2026 · 16 elapsed days

Latest conform: cna030_v03.mov



cna040

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	adam	done

Historical assignments: adam, jack

Latest recorded approval / done: 19 Jan 2026

65 recorded events · 9 active dates
06 Jan – 22 Jan 2026 · 16 elapsed days

Latest conform: cna040_v03.mov



cna050

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	adam	done

Historical assignments: adam, jack

Latest recorded approval / done: 19 Jan 2026

28 recorded events · 7 active dates
06 Jan – 22 Jan 2026 · 16 elapsed days

Latest conform: cna050_v06.mov



cna060

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	adam	done

Historical assignments: adam, jack

Latest recorded approval / done: 19 Jan 2026

30 recorded events · 8 active dates
06 Jan – 23 Jan 2026 · 17 elapsed days

Latest conform: cna060_v03.mov



cna070

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	adam	done

Historical assignments: adam, jack

Latest recorded approval / done: 19 Jan 2026

28 recorded events · 9 active dates
06 Jan – 22 Jan 2026 · 16 elapsed days

Latest conform: cna070_v04.mov

Considerations B2

5 shots · 1 hidden · 31 production events

4 tasks in other open states.



cnb010

Recorded work: “Match move”.

Task / note	Assigned to	Status
Match move	jack	unassigned

Historical assignments: jack

18 recorded events · 4 active dates
06 Jan – 29 Jan 2026 · 23 elapsed days


Latest conform: cnb010_v03.mov



cnb020 / HIDDEN

No task-level work description is recorded.

7 recorded events · 1 active date
06 Jan – 06 Jan 2026 · 0 elapsed days



cnb030


Recorded work: “Match move”.

Task / note	Assigned to	Status
Match move	jack	unassigned

Historical assignments: jack

7 recorded events · 2 active dates
06 Jan – 29 Jan 2026 · 23 elapsed days

Latest conform: cnb030_v01.mov

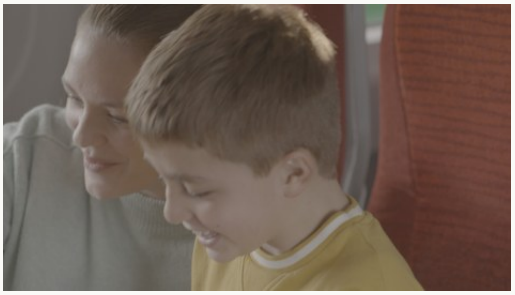

cnb040

Recorded work: “Match move”.

Task / note	Assigned to	Status
Match move	jack	unassigned

Historical assignments: jack

10 recorded events · 4 active dates
06 Jan – 11 Feb 2026 · 36 elapsed days

Latest conform: cnb040_v02.mov



cnb050

Recorded work: “Match move”.

Task / note	Assigned to	Status
Match move	jack	unassigned

Historical assignments: jack

8 recorded events · 2 active dates
06 Jan – 29 Jan 2026 · 23 elapsed days

Latest conform: cnb050_v01.mov

new shots

9 shots · 1 hidden · 129 production events

6 tasks done; 1 task awaiting approval; 10 tasks in other open states.



sho010

Recorded work: “Match move” and “Comp”.

Task / note	Assigned to	Status
Match move	jack	done
Comp	Prateek	done

Historical assignments: Prateek, jack

Latest recorded approval / done: 14 Jan 2026

22 recorded events · 4 active dates
09 Jan – 15 Jan 2026 · 6 elapsed days

Latest conform: sho010_v08.mov (MOV)



sho020

Recorded work: “Camera match” and “Comp”.

Task / note	Assigned to	Status
Camera match	adam	done
Comp — flickery	Prateek	waiting for approval

Historical assignments: Prateek, adam, jack

Latest recorded approval / done: 14 Jan 2026

27 recorded events · 6 active dates
09 Jan – 19 Jan 2026 · 10 elapsed days

Latest conform: sho020_v12.mov (MOV)



sho030

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 15 Jan 2026

11 recorded events · 3 active dates
09 Jan – 15 Jan 2026 · 6 elapsed days



sho040

Recorded work: “Comp” and “Camera match”.

Task / note	Assigned to	Status
Comp	Prateek	done
Camera match	adam	done

Historical assignments: Prateek, adam

Latest recorded approval / done: 14 Jan 2026

18 recorded events · 6 active dates
09 Jan – 29 Jan 2026 · 20 elapsed days

Latest conform: sho040_v07.mov (MOV)



sho050

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	Prateek	in progress

Historical assignments: Prateek

18 recorded events · 5 active dates
09 Jan – 27 Jan 2026 · 18 elapsed days

Latest conform: sho050_v09.mov



sho060

Recorded work: “Match move”, “Roto” and “Comp”.

Task / note	Assigned to	Status
Match move — magic pie	Unassigned	unassigned
Roto	Unassigned	unassigned
Comp	paul_greenwood	in progress

Historical assignments: outsource, paul_greenwood

26 recorded events · 6 active dates
09 Jan – 20 Mar 2026 · 70 elapsed days

Latest conform: sho060_v09_####.exr 1050-1087



sho070

Recorded work: “Roto”, “Comp” and “sign”.

Task / note	Assigned to	Status
Roto	jack	unassigned
Comp	jack	unassigned
sign	Unassigned	unassigned

Historical assignments: jack

22 recorded events · 7 active dates
09 Jan – 26 Jan 2026 · 17 elapsed days

Latest conform: sho070_v08_####.exr 1001-1135



sho080

Recorded work: “Roto”, “Comp” and “sign”.

Task / note	Assigned to	Status
Roto	jack	unassigned
Comp	jack	unassigned
sign	Unassigned	unassigned

Historical assignments: jack

20 recorded events · 8 active dates
09 Jan – 26 Jan 2026 · 17 elapsed days

Latest conform: sho080_v06_####.exr 1001-1160



sho090 / HIDDEN

No task-level work description is recorded.

3 recorded events · 2 active dates
09 Jan – 12 Jan 2026 · 3 elapsed days

EleanorCore

13 shots · 0 hidden · 175 production events

1 task approved; 12 tasks done.



con010

Recorded work: “Split plate”.


Task / note	Assigned to	Status
Split plate	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 05 Feb 2026

17 recorded events · 6 active dates
20 Jan – 17 Feb 2026 · 28 elapsed days

Latest conform: con010_v11.mov



con020

Recorded work: “Phone Screne tracking”.

Task / note	Assigned to	Status
Phone Screne tracking	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 13 Feb 2026

18 recorded events · 10 active dates
20 Jan – 17 Feb 2026 · 28 elapsed days

Latest conform: con020_v06.mov



con030

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 13 Feb 2026

24 recorded events · 6 active dates
20 Jan – 17 Feb 2026 · 28 elapsed days

Latest conform: con030_v05.mov



con040

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 13 Feb 2026

22 recorded events · 7 active dates
20 Jan – 17 Feb 2026 · 28 elapsed days

Latest conform: con040_v05.mov



con050

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 13 Feb 2026

20 recorded events · 7 active dates
20 Jan – 17 Feb 2026 · 28 elapsed days

Latest conform: con050_v04.mov



con060

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 13 Feb 2026

22 recorded events · 7 active dates
20 Jan – 17 Feb 2026 · 28 elapsed days

Latest conform: con060_v05.mov



con070

Recorded work: “Comp”.


Task / note	Assigned to	Status
Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 13 Feb 2026

24 recorded events · 8 active dates
20 Jan – 17 Feb 2026 · 28 elapsed days

Latest conform: con070_v07.mov



con080

Recorded work: “Comp”.


Task / note	Assigned to	Status
Comp	Prateek	approved

Historical assignments: Prateek

Latest recorded approval / done: 13 Feb 2026

22 recorded events · 8 active dates
20 Jan – 18 Feb 2026 · 29 elapsed days

Latest conform: con080_v03.mov



con090

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 13 Feb 2026

23 recorded events · 7 active dates
20 Jan – 18 Feb 2026 · 29 elapsed days

Latest conform: con090_v05.mov



con100

Recorded work: “Keying, roto & Comp”.

Task / note	Assigned to	Status
Keying, roto & Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 05 Feb 2026

16 recorded events · 7 active dates
20 Jan – 13 Feb 2026 · 24 elapsed days

Latest conform: con100_v04.mov



con110

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 05 Feb 2026

19 recorded events · 7 active dates
20 Jan – 18 Feb 2026 · 29 elapsed days

Latest conform: con110_v05.mov



con120

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 05 Feb 2026

22 recorded events · 9 active dates
20 Jan – 23 Feb 2026 · 34 elapsed days

Latest conform: con120_v02.mov



con130

Recorded work: “Keying, roto & Comp”.

Task / note	Assigned to	Status
Keying, roto & Comp	Prateek	done

Historical assignments: Prateek

Latest recorded approval / done: 13 Feb 2026

19 recorded events · 8 active dates
20 Jan – 13 Feb 2026 · 24 elapsed days

Latest conform: con130_v04.mov

Tips

16 shots · 0 hidden · 193 production events

1 task approved; 21 tasks done; 1 task awaiting approval; 4 tasks in other open states.



tip010

Recorded work: “maybe tracked”.

Task / note	Assigned to	Status
maybe tracked	Unassigned	unassigned

14 recorded events · 6 active dates
22 Jan – 17 Feb 2026 · 26 elapsed days

Latest conform: tip010_v05.mov



tip020

Recorded work: “Match move”, “Comp”, “BG” and “BG_REVERSE”.


Task / note	Assigned to	Status
Match move [hidden]	jack	done
Comp [hidden]	Prateek	done
BG — RENDERED [hidden]	paul_greenwood	done
BG_REVERSE	paul_greenwood	approved

Historical assignments: Prateek, jack, paul_greenwood

Latest recorded approval / done: 24 Feb 2026

38 recorded events · 11 active dates
22 Jan – 25 Feb 2026 · 34 elapsed days

Latest conform: tip020_v05.mov



tip030

Recorded work: “maybe tracked”.

Task / note	Assigned to	Status
maybe tracked	Unassigned	done

Latest recorded approval / done: 17 Feb 2026

8 recorded events · 4 active dates
22 Jan – 17 Feb 2026 · 26 elapsed days

Latest conform: tip030_v03.mov



tip040

Recorded work: “Match move”, “Comp” and “CG Background”.


Task / note	Assigned to	Status
Match move	jack	done
Comp	Prateek	done
CG Background	paul_greenwood	done

Historical assignments: Prateek, jack, paul_greenwood

Latest recorded approval / done: 12 Feb 2026

29 recorded events · 8 active dates
22 Jan – 25 Feb 2026 · 34 elapsed days

Latest conform: tip040_v04.mov



tip050

Recorded work: “Match move”, “Comp” and “CG Background”.


Task / note	Assigned to	Status
Match move	jack	done
Comp	Prateek	done
CG Background	paul_greenwood	done

Historical assignments: Prateek, jack, paul_greenwood

Latest recorded approval / done: 11 Feb 2026

32 recorded events · 9 active dates
22 Jan – 25 Feb 2026 · 34 elapsed days

Latest conform: tip050_v06.mov



tip060

No task-level work description is recorded.

7 recorded events · 4 active dates
22 Jan – 17 Feb 2026 · 26 elapsed days

Latest conform: tip060_v03.mov



tip070

No task-level work description is recorded.

5 recorded events · 4 active dates
22 Jan – 17 Feb 2026 · 26 elapsed days

Latest conform: tip070_v02.mov



tip080

Recorded work: “Match move” and “Comp”.


Task / note	Assigned to	Status
Match move	jack	done
Comp	Prateek	done

Historical assignments: Prateek, jack

Latest recorded approval / done: 25 Feb 2026

21 recorded events · 8 active dates
22 Jan – 25 Feb 2026 · 34 elapsed days

Latest conform: tip080_v05.mov



tip090

Recorded work: “Match move”, “Comp” and “BG_RE_RENDER”.

Task / note	Assigned to	Status
Match move	jack	done
Comp	Prateek	done
BG_RE_RENDER — ADDED MORE TREES	paul_greenwood	done

Historical assignments: Prateek, jack, paul_greenwood

Latest recorded approval / done: 25 Feb 2026

34 recorded events · 10 active dates
22 Jan – 26 Feb 2026 · 35 elapsed days

Latest conform: tip090_v08.mov




tip100

Recorded work: “Back carriage” and “match still”.

Task / note	Assigned to	Status
Back carriage	Unassigned	unassigned
match still	Unassigned	unassigned

7 recorded events · 5 active dates
22 Jan – 17 Feb 2026 · 26 elapsed days

Latest conform: tip100_v02.mov




tip110

No task-level work description is recorded.

6 recorded events · 4 active dates
22 Jan – 17 Feb 2026 · 26 elapsed days

Latest conform: tip110_v03.mov



tip120

Recorded work: “Match move” and “Comp”.

Task / note	Assigned to	Status
Match move	jack	done
Comp	Prateek	waiting for approval

Historical assignments: Prateek, jack

Latest recorded approval / done: 05 Feb 2026

20 recorded events · 8 active dates
22 Jan – 26 Feb 2026 · 35 elapsed days

Latest conform: tip120_v03_####.exr 1001-1110




tip130

No task-level work description is recorded.

7 recorded events · 4 active dates
22 Jan – 17 Feb 2026 · 26 elapsed days

Latest conform: tip130_v04.mov



tip140

Recorded work: “Match move” and “Comp”.


Task / note	Assigned to	Status
Match move	jack	done
Comp	Prateek	done

Historical assignments: Prateek, jack

Latest recorded approval / done: 16 Feb 2026

22 recorded events · 9 active dates
22 Jan – 25 Feb 2026 · 34 elapsed days

Latest conform: tip140_v07.mov



tip150

Recorded work: “Match move”, “Comp” and “CG Background”.

Task / note	Assigned to	Status
Match move	jack	done
Comp	Prateek	done
CG Background	paul_greenwood	done

Historical assignments: Prateek, jack, paul_greenwood

Latest recorded approval / done: 12 Feb 2026

34 recorded events · 11 active dates
22 Jan – 04 Mar 2026 · 41 elapsed days

Latest conform: tip150_v11.mov



tip160

Recorded work: “Match move”.

Task / note	Assigned to	Status
Match move	Unassigned	unassigned

6 recorded events · 5 active dates
22 Jan – 17 Feb 2026 · 26 elapsed days

Latest conform: tip160_v02.mov

SpendTheDayWithMe

33 shots · 21 hidden · 48 production events

1 task in other open states.



spd010

Recorded work: “Comp”.

Task / note	Assigned to	Status
Comp [hidden]	Prateek	in progress

Historical assignments: Prateek

13 recorded events · 8 active dates
26 Jan – 16 Mar 2026 · 49 elapsed days



spd020

No task-level work description is recorded.


12 recorded events · 5 active dates
26 Jan – 16 Mar 2026 · 49 elapsed days



spd030

No task-level work description is recorded.


10 recorded events · 5 active dates
26 Jan – 16 Mar 2026 · 49 elapsed days



spd040 / HIDDEN

No task-level work description is recorded.

3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd050 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd060 / HIDDEN

No task-level work description is recorded.

3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd070 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd080 / HIDDEN

No task-level work description is recorded.

3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd090 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd100

No task-level work description is recorded.


11 recorded events · 7 active dates
26 Jan – 16 Mar 2026 · 49 elapsed days



spd110

No task-level work description is recorded.


7 recorded events · 3 active dates
26 Jan – 19 Feb 2026 · 24 elapsed days



spd120 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd130 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd140 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd150 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd160 / HIDDEN

No task-level work description is recorded.


4 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd170 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd180 / HIDDEN

No task-level work description is recorded.

3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd190 / HIDDEN

No task-level work description is recorded.

3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd200

No task-level work description is recorded.


10 recorded events · 5 active dates
26 Jan – 12 Mar 2026 · 45 elapsed days



spd210

No task-level work description is recorded.


10 recorded events · 6 active dates
26 Jan – 16 Mar 2026 · 49 elapsed days



spd220 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd230

No task-level work description is recorded.


5 recorded events · 2 active dates
26 Jan – 18 Feb 2026 · 23 elapsed days



spd240

No task-level work description is recorded.


8 recorded events · 3 active dates
26 Jan – 23 Feb 2026 · 28 elapsed days



spd250 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd260 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd270 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd280 / HIDDEN

No task-level work description is recorded.

3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd290 / HIDDEN

No task-level work description is recorded.


3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd300

No task-level work description is recorded.


9 recorded events · 3 active dates
26 Jan – 19 Feb 2026 · 24 elapsed days



spd310 / HIDDEN

No task-level work description is recorded.

3 recorded events · 2 active dates
26 Jan – 17 Feb 2026 · 22 elapsed days



spd320

No task-level work description is recorded.

6 recorded events · 2 active dates
26 Jan – 18 Feb 2026 · 23 elapsed days



spd330

No task-level work description is recorded.

7 recorded events · 3 active dates
26 Jan – 19 Feb 2026 · 24 elapsed days
